

ID	Task Name	Duration	Start	Finish	Predeces	Resource Names
1	**Construction**	**240 days**	**Sun 03/11/24**	**Tue 21/10/25**		
2	**Phase 1**	**35 days**	**Sun 03/11/24**	**Sun 22/12/24**		
3	Mobilization at S	3 days	Sun 03/11/24	Tue 05/11/24		Franklin Clinton
4	Surveying and La	3 days	Wed 06/11/24	Sun 10/11/24	3	Lester Crest
5	Milestone: Completion of Site	0 days	Sun 10/11/24	Sun 10/11/24	4	
6	Excavation	5 days	Mon 11/11/24	Sun 17/11/24	4	Franklin Clinton,L
7	Footing	6 days	Mon 18/11/24	Mon 25/11/24	6	Lester Crest,Conc
8	Column upto Plinth Level	6 days	Tue 26/11/24	Tue 03/12/24	7	Franklin Clinton
9	Backfilling in Foc	2 days	Wed 04/12/24	Thu 05/12/24	8	Lester Crest,Conc
10	Plinth Beam	4 days	Sun 08/12/24	Wed 11/12/24	9	Lester Crest
11	Earth Filling in Plinth Level	3 days	Thu 12/12/24	Tue 17/12/24	10	Franklin Clinton
12	CC Filling with P(	3 days	Wed 18/12/24	Sun 22/12/24	11	Franklin Clinton
13	**Phase 2**	**50 days**	**Mon 23/12/24**	**Tue 04/03/25**	**2**	
14	1st Floor Slab	10 days	Mon 23/12/24	Tue 07/01/25		Franklin Clinton
15	Brick Work at First Floor	13 days	Wed 08/01/25	Sun 26/01/25	14	Lester Crest
16	Internal Plaster a	8 days	Mon 27/01/25	Wed 05/02/25	15	Michael De Santa
17	Flooring Work G	8 days	Mon 27/01/25	Wed 05/02/25	15	Franklin Clinton

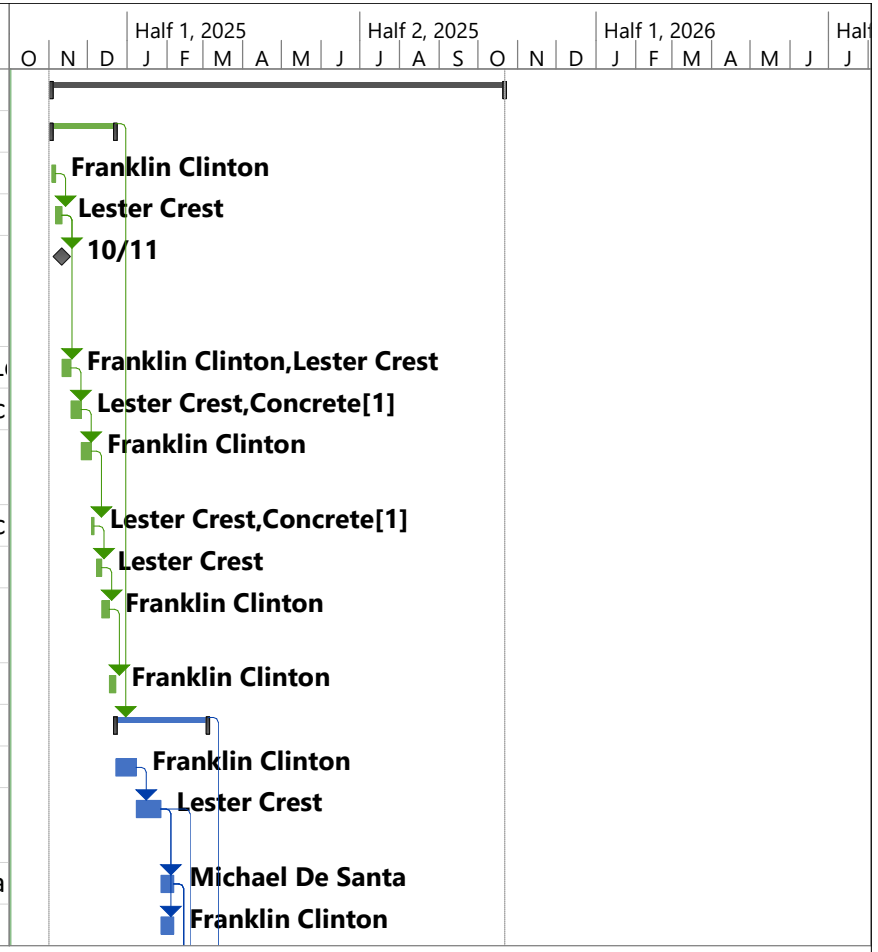

Project: Construction of a hous
Date: Wed 02/10/24

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Critical	
Project Summary	Manual Summary	Critical Split	
Inactive Task	Start-only	Progress	
Inactive Milestone	Finish-only	Manual Progress	


ID	Task Name	Duration	Start	Finish	Predeces	Resource Names
18	Door and Window Work	6 days	Thu 06/02/25	Thu 13/02/25	16	Michael De Santa
19	Internal Painting	6 days	Thu 06/02/25	Thu 13/02/25	16	Paint[1],Franklin (
20	Column 1st to 2nd Floor	9 days	Thu 06/02/25	Tue 18/02/25	16	Lester Crest
21	2nd Floor Slab	10 days	Wed 19/02/25	Tue 04/03/25	15,20	Michael De Santa,
22	**Phase 3**	**65 days**	**Wed 05/03/25**	**Mon 16/06/25**	**13**	
23	2nd Floor Slab	10 days	Wed 05/03/25	Tue 18/03/25		Lester Crest,Conc
24	Milestone: Completion of 2nd Floor Slab	0 days	Tue 18/03/25	Tue 18/03/25	23	
25	Brick Work at First Floor	20 days	Wed 19/03/25	Thu 24/04/25	23	Michael De Santa
26	Internal Plaster at GF	10 days	Sun 27/04/25	Mon 12/05/25	25	Franklin Clinton
27	Flooring Work G	10 days	Sun 27/04/25	Mon 12/05/25	25	Michael De Santa
28	Door and Windo	9 days	Tue 13/05/25	Sun 25/05/25	26	Franklin Clinton
29	Internal Painting	9 days	Tue 13/05/25	Sun 25/05/25	26	Lester Crest
30	Column 2nd to 3rd Floor	13 days	Tue 13/05/25	Thu 29/05/25	26	Michael De Santa
31	3rd Floor Slab	10 days	Sun 01/06/25	Mon 16/06/25	25,30	Lester Crest,Frank
32	**Phase 4**	**90 days**	**Tue 17/06/25**	**Tue 21/10/25**	**22**	
33	Brick Work at 2nd Floor	10 days	Tue 17/06/25	Mon 30/06/25		Franklin Clinton

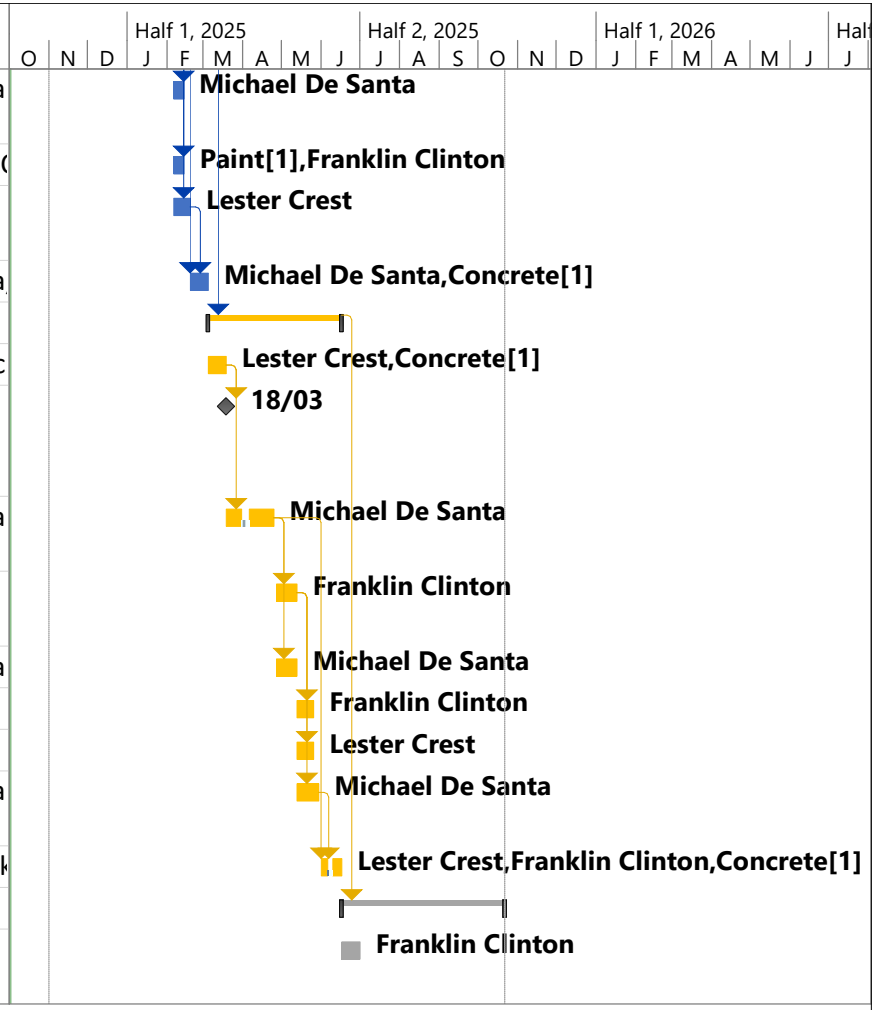

Project: Construction of a hous
Date: Wed 02/10/24

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Critical	
Project Summary	Manual Summary	Critical Split	
Inactive Task	Start-only	Progress	
Inactive Milestone	Finish-only	Manual Progress	

ID	Task Name	Duration	Start	Finish	Predeces	Resource Names
34	Internal Plaster at GF	8 days	Tue 17/06/25	Thu 26/06/25		Michael De Santa
35	Flooring Work G	8 days	Tue 17/06/25	Thu 26/06/25		Lester Crest
36	Door and Window Work	7 days	Sun 29/06/25	Tue 08/07/25	34	Lester Crest
37	Internal Painting	6 days	Wed 09/07/25	Wed 16/07/25	36	Franklin Clinton
38	Column 3rd to Terrace	10 days	Thu 17/07/25	Wed 30/07/25	37	Lester Crest
39	Brick Work at 3rd Floor	10 days	Thu 17/07/25	Wed 30/07/25	37	Michael De Santa
40	Internal Plaster at 3rd Floor	10 days	Thu 31/07/25	Wed 13/08/25	39	Lester Crest
41	Flooring Work	12 days	Thu 14/08/25	Sun 31/08/25	40	Franklin Clinton
42	Internal Painting	7 days	Mon 01/09/25	Tue 09/09/25	41	Lester Crest,Paint
43	Parapet Wall	7 days	Wed 10/09/25	Thu 18/09/25	42	Michael De Santa
44	External Plaster	8 days	Sun 21/09/25	Tue 30/09/25	43	Lester Crest
45	Terrace Water Proofing	7 days	Wed 01/10/25	Thu 09/10/25	44	Franklin Clinton
46	Finish and Hand	6 days	Sun 12/10/25	Sun 19/10/25	45	Franklin Clinton,L
47	Milestone: Final inspection done	0 days	Sun 19/10/25	Sun 19/10/25	46	
48	Handover	2 days	Mon 20/10/25	Tue 21/10/25	46	Michael De Santa
49	Milestone: Project	0 days	Tue 21/10/25	Tue 21/10/25	48	

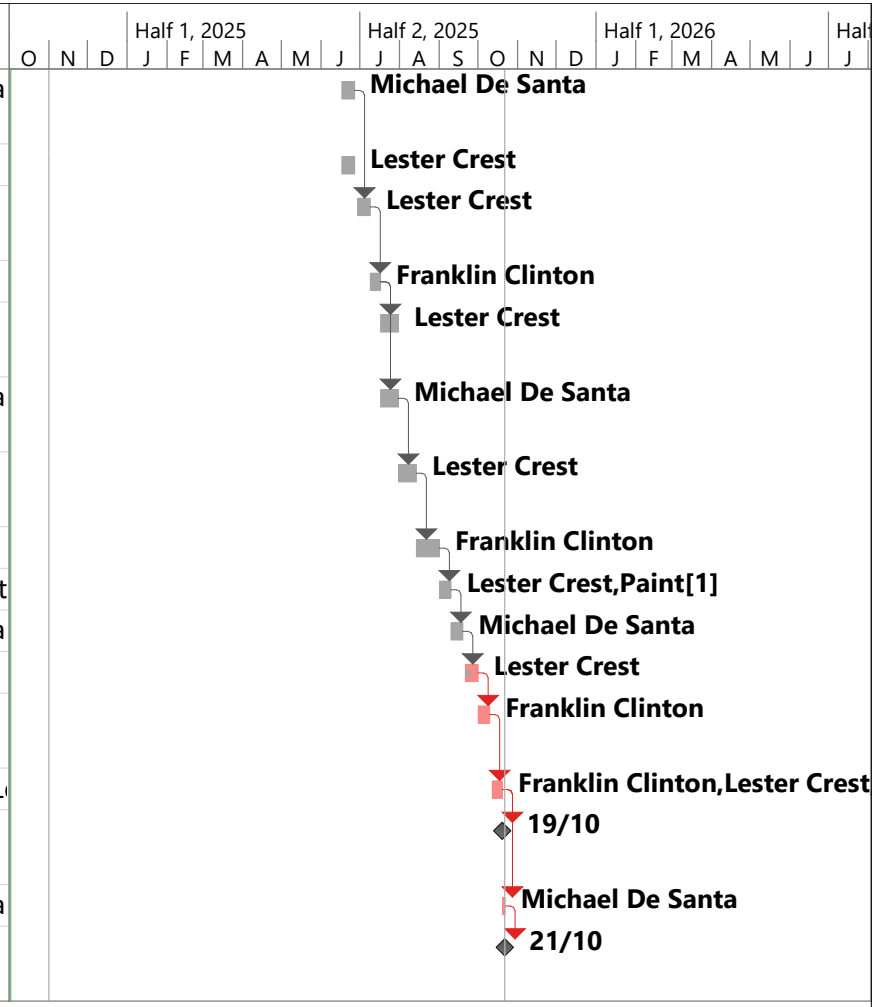

Project: Construction of a hous
Date: Wed 02/10/24

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Critical	
Project Summary	Manual Summary	Critical Split	
Inactive Task	Start-only	Progress	
Inactive Milestone	Finish-only	Manual Progress	
